



AGENDA REPORT

Meeting Date: October 21, 2014
Item Number: D-12
To: Honorable Mayor & City Council
From: Mark Cuneo, City Engineer
Juan Martinez, Civil Engineer
Subject: ACCEPTANCE OF THE CONTRACT WORK FOR THE 2012-2013 STREET RESURFACING – VARIOUS LOCATIONS BY ALL AMERICAN ASPHALT, IN THE FINAL AMOUNT OF \$2,824,499.25; AND
AUTHORIZATION OF CITY CLERK TO RECORD NOTICE OF COMPLETION
Attachments: 1. Location Map
2. Notice of Completion

RECOMMENDATION

Staff recommends that the City Council move to accept the described work with All American Asphalt, and authorize the City Clerk to record the attached Notice of Completion.

INTRODUCTION

This report provides information to the City Council for acceptance of the contract work in the final amount of \$2,824,499.25 and authorization for the recordation of the Notice of Completion by the City Clerk with the Los Angeles County Recorder.

DISCUSSION

On April 11, 2013, a contract in the amount of \$3,267,000 was awarded to All American Asphalt on the basis of sealed competitive bids received after public advertising for the 2012-2013 Street Resurfacing – Various Locations project.

As part of the City's 5-year Street Resurfacing Capital Improvement Program (CIP), streets with Pavement Index (PI) below 60, showing deteriorated condition, were selected for the FY2012-2013 resurfacing project. These streets were repaired and rehabilitated, increasing the structural serviceability life of the pavement by at least 25

years. Pavement Index values were obtained from the network inventory of streets using field reconnaissance. Data collected on the condition of the streets and alleys is input and analyzed using a standard pavement management software called Micro Paver. The plans and specifications for the project were approved with respect to design criteria by a Professional Civil Engineer licensed in the State of California.

All American Asphalt mobilized and construction commenced on July 3, 2013. Engineering Division personnel inspected all the work and are satisfied that the work was completed according to the contract documents approved for this project. The 5.4 miles of streets and 2.9 miles of alleys paved as part of this project are as follows:

STREET NAME	FROM	TO
ALLEY N/OF OLYMPIC BLVD	REEVES DR	DOHENY DR
ALLEY S/OF OLYMPIC BLVD	ROXBURY DR	CAMDEN DR
ALLEY W/OF BEVERLY DR	CITY LIMITS	WILSHIRE BLVD
ALLEY W/OF CAMDEN DR	CITY LIMITS	WILSHIRE BLVD
ALLEY W/OF CLARK DR	WHITWORTH DR	WILSHIRE BLVD
ALLEY W/OF DOHENY DR	WHITWORTH DR	WILSHIRE BLVD
ALLEY W/OF EL CAMINO	RODEO DR	OLYMPIC BLVD
ALEXIS PL	TROUSDALE PL	EOP
ARKELL DR	LOMA VISTA DR	HAYNES AVE
ARKELL DR	HAYNES AVE	CARLA RIDGE
BARRIE DR	HILLCREST RD	MAYTON PL
BEDFORD DR	WILSHIRE BLVD	SANTA MONICA BLVD SOUTH
BEVERLY DR	COLDWATER CANYON	CITY LIMITS
BEVERLY DR	DAYTON WAY	SANTA MONICA BLVD SOUTH
BURK PL	CARLA RIDGE	EOP
CARLA LN	CARLA RIDGE	EOP
CARLA RIDGE	EOP	LOMA VISTA DR
CARLA RIDGE	LOMA VISTA DR	CITY LIMITS
CASTLE PL	LOMA VISTA DR	EOP
CHALETTE DR	LOMA VISTA DR	CARLA RIDGE
CHRIS PL	LOMA VISTA DR	EOP
CLINTON PL	CARLA RIDGE	EOP
COLE PL	CARLA RIDGE	EOP
CORD CIRCLE	DOHENY RD	EOP
ENDRINO PL	CARLA RIDGE	EOP
GALE DR	GREGORY WAY	WILSHIRE BLVD
HAMEL DR	CHARLEVILLE BLV	WILSHIRE BLVD
HAMILTON DR	WILSHIRE BLVD	SAN VICENTE BL
HAYNES AVE	CARLA RIDGE	ARKELL DR
LESLIE LN	LOMA VISTA DR	EOP
MARTIN LANE	LOMA VISTA DR	EOP
MAYTOR PL	CUL DE SAC	CUL DE SAC

SHADOW HILL WAY BEVERLY DR SUNNYVALE WAY

STREET NAME	FROM	TO
SUTTON WAY	BEVERLY DR	EOP
TOWER DR	GREGORY WAY	WILSHIRE BLVD
TROUSDALE PL	ALEXIS PL	EOP
TROUSDALE PL	LOMA VISTA DR	ALEXIS PL
USHER PL	LOMA VISTA DR	CARLA RIDGE
VICK PL	ARKELL DR	EOP
WALKER DR	CARLA RIDGE	EOP
WILLIAMS LN	CARLA RIDGE	EOP

The alley West of Oakhurst Dr. from Olympic Blvd to Wilshire Blvd was removed from this project due to an upcoming Southern California Edison project. Linda Crest from Coldwater Canyon to City limits was also removed due to an upcoming water project.

The following two additional streets segments were added to this project in lieu of the aforementioned deleted location:

STREET NAME	FROM	TO
BEVERLY DR	LAUREL WAY	COLDWATER CANYON
REXFORD DR	WILSHIRE BLVD	SANTA MONICA BLVD SOUTH
REXFORD DR	SUNSET BLVD	BEVERLY DR
THIRD STREET	CIVIC CENTER DR	OAKHURST DR

FISCAL IMPACT

The original contract purchase order, which included a \$297,000 contingency allowance, was for \$3,267,000. The current amount invoiced and paid to All American Asphalt on the contract is \$2,683,274.28 with a balance of \$141,224.97 due to be paid 35 days after the recordation of the Notice of Completion for a total project cost of \$2,824,499.25

David Lightner 
Approved By

Attachment 1



PUBLIC WORKS & TRANSPORTATION


STREET MAP OF THE CITY OF BEVERLY HILLS

DEPARTMENT OF PUBLIC WORKS AND TRANSPORTATION
ENGINEERING DIVISION

2012/2013 Street Resurfacing Project

DEPARTMENT OF PUBLIC WORKS AND TRANSPORTATION
LEGEND

- Completed Streets and Alleys
- Completed Bike lane

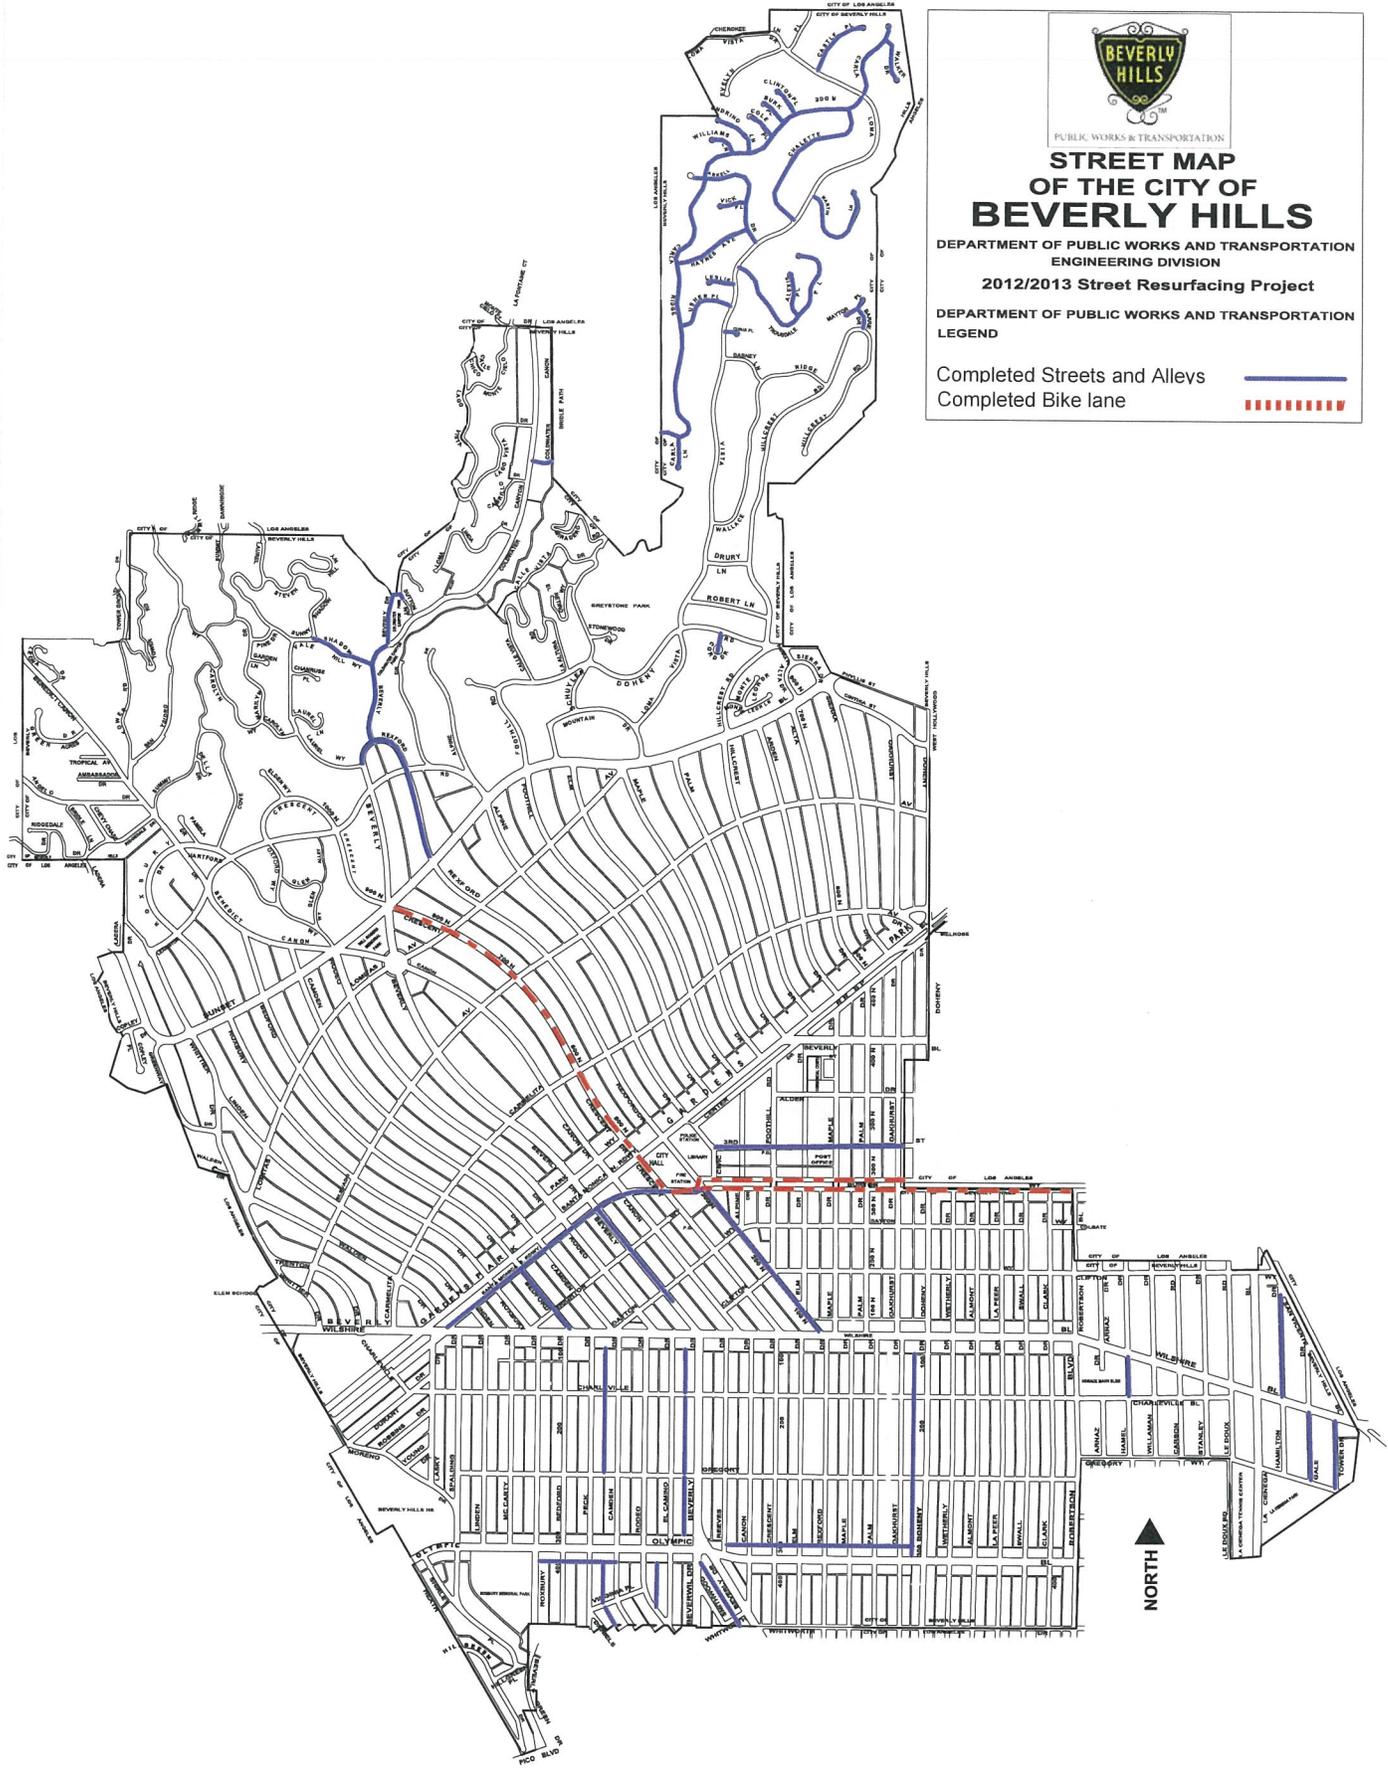

Attachment 2

THIS DOCUMENT IS OFFICIAL BUSINESS
OF THE CITY OF BEVERLY HILLS AND
ENTITLED TO FREE RECORDING UNDER
SECTION 6103 OF THE GOVERNMENT CODE

Requested by _____

AFTER RECORDING MAIL TO:

CITY CLERK'S OFFICE
Room 290, City Hall
455 North Rexford Drive
Beverly Hills, CA 90210

Space above this line for recorder's use

NOTICE OF COMPLETION

Notice is hereby given that:

1. The undersigned is owner of the interest or estate stated below in the property hereinafter described.
2. The full name of the undersigned is **City of Beverly Hills**
3. The full address of the undersigned is **455 North Rexford Drive, Beverly Hills, CA 90210**
4. The nature of the title of the undersigned is: **In fee.**
5. The full names and addresses of all persons who hold title with the undersigned are:
None
6. A work of improvement on the property hereinafter described was completed on October 27, 2014
7. The name of the contractor, if any, for such work of improvement was
All American Asphalt
8. The property on which said work of improvement was completed is in the City of **Beverly Hills**, County of **Los Angeles**, State of **California**, as is described as:
2012-2013 Street Resurfacing – Various Locations within the City of Beverly Hills
9. The street address of said property is None

Dated: _____

STATE OF CALIFORNIA	}	Signature of	}
COUNTY OF LOS ANGELES	}	Owner or Owners	} _____

Byron Pope _____, being duly sworn, says: That he is the City Clerk _____ of the **City of Beverly Hills**, the corporation that executed the foregoing notice as owner of the aforesaid interest or estate in the property therein described; that he makes this verification of behalf of said corporation; that he has read said notice and knows the contents thereof, and that the facts therein stated are true.

Signature of
Corporate Officer
Named Above X _____
